











ID	Task Name	Duration	Start	Finish	Predecessor	FSS	T	TFS
1	<b>START</b>	0 days	Wed 01.04.09	Wed 01.04.09				
2	<b>1. WP1 PROJECT MANAGEMENT</b>	499 days?	Tue 17.02.09	Fri 14.01.11				
3	<b>1.1.Establishment of Project Steering Committee</b>	438 days?	Tue 17.02.09	Thu 21.10.10				
4	1.1.1. Establishment of PTs (Project Teams) in their own country	9 days	Tue 17.02.09	Fri 27.02.09				
5	1.1.2. Steering Committee in TURKEY (SCM 1)	1 day?	Fri 01.05.09	Fri 01.05.09	17			
6	1.1.3. Steering Committee Meeting in Spain (SCM 2)	3 days	Fri 07.05.10	Tue 11.05.10	94FS+11 c			
7	1.1.4 Last Steering Committee Meeting in Turkey (Ankara) (SCM 3)	4 days	Mon 18.10.10	Thu 21.10.10				
8	1.1.5 Draft a "quality road map"	15 days	Fri 22.05.09	Thu 11.06.09	17FS+15 c			
9	<b>1.2 REPORT</b>	430 days	Mon 25.05.09	Fri 14.01.11				
10	1.2.1 Preparing the project progress reports	20 days	Mon 25.05.09	Fri 19.06.09				
11	1.2.2 Interim Report	15 days	Mon 07.12.09	Fri 25.12.09				
12	1.2.3 Preparing the project progress reports	15 days	Mon 24.05.10	Fri 11.06.10				
13	1.2.4 Preparing a final technical and financial report	20 days	Mon 20.12.10	Fri 14.01.11				
14	<b>2. WP2.VALORISATION</b>	426 days	Wed 01.04.09	Wed 17.11.10				
15	<b>2.1 Organization of the Kick of Meeting</b>	22 days	Wed 01.04.09	Thu 30.04.09				
16	2.1.1 Preparation of Kick of Meeting	15 days	Wed 01.04.09	Tue 21.04.09	1			
17	2.1.2 Kick of meeting	2 days	Wed 29.04.09	Thu 30.04.09	16;21			
18	<b>2.2 Brochures and Posters</b>	19 days	Wed 01.04.09	Mon 27.04.09				
19	2.2.1 Preparation of contents for brochures and posters	5 days	Wed 01.04.09	Tue 07.04.09	1			
20	2.2.2. Translation of the brochures and posters	6 days	Wed 08.04.09	Wed 15.04.09	19			
21	2.2.3 Publication of the brochures and posters	8 days	Thu 16.04.09	Mon 27.04.09	20			
22	<b>2.3 WEBSITE</b>	20 days	Wed 01.04.09	Tue 28.04.09				
23	2.3.1 Preparation of the content of the web-site	10 days	Wed 01.04.09	Tue 14.04.09	1			
24	2.3.2 Establishment of Web-site	10 days	Wed 15.04.09	Tue 28.04.09	23			
25	<b>2.4 INTRANET</b>	20 days	Wed 01.04.09	Tue 28.04.09				
26	2.4.1.Establishment of the intranet	20 days	Wed 01.04.09	Tue 28.04.09	1			
27	<b>2.5 Dissemination Meeting</b>	15 days	Thu 28.10.10	Wed 17.11.10	105FS+60			
28	<b>3.WP3. ADAPTATION OF SME-TIC METHODOLOGIES AND OUTPUTS</b>	88 days	Thu 27.08.09	Mon 28.12.09				
29	<b>3.1. Preparation of training programmes</b>	78 days	Thu 27.08.09	Mon 14.12.09				
30	3.1.1 Drafting the methodology of the training itinerary based on VQs	20 days	Thu 27.08.09	Wed 23.09.09	17;40			
31	3.1.2 Revision of the methodology of the training itinerary based on SME's needs	10 days	Mon 02.11.09	Fri 13.11.09	30;53			
32	3.1.3 Finalization and adaptation of the methodology of the training itinerary	20 days	Mon 16.11.09	Fri 11.12.09	31			
33	3.1.4 Sharing the adopted version of itinerary with San Valero	1 day	Mon 14.12.09	Mon 14.12.09	32			
34	<b>3.2 Reporting WP 3</b>	10 days	Tue 15.12.09	Mon 28.12.09	33			
35	<b>4. WP4. DEVELOPMENT OF VQ'S FOR "DATA SECURITY SKILLED WORKERS"FOR SME'S</b>	88 days	Mon 29.06.09	Wed 28.10.09				
36	<b>4.1.Common Vocational Qualifications</b>	43 days	Mon 29.06.09	Wed 26.08.09				
37	4.1.1 Development of first draft of 3 Common VQ's	18 days	Mon 29.06.09	Wed 22.07.09	17FS+41 c			
38	4.1.2 Feedbacks for common VQ's from partners	5 days	Thu 23.07.09	Wed 29.07.09	37			
39	4.1.3 Revision of common vocational qualifications	10 days	Thu 30.07.09	Wed 12.08.09	38			
40	4.1.4 Finalization of the common vocational qualifications	10 days	Thu 13.08.09	Wed 26.08.09	39			
41	<b>4.2 Country Specific Qualifications</b>	25 days	Thu 27.08.09	Wed 30.09.09				
42	4.2.1 Development of country specific qualifications	10 days	Thu 27.08.09	Wed 09.09.09	40			
43	4.2.2 Feedbacks for country specific qualification from partners	5 days	Thu 10.09.09	Wed 16.09.09	42			
44	4.2.3.Revision of country specific qualifications	5 days	Thu 17.09.09	Wed 23.09.09	43			
45	4.2.4. Finalization of the country specific qualification	5 days	Thu 24.09.09	Wed 30.09.09	44			
46	<b>4.3. Translation of finalized professional qualifications of the project</b>	10 days	Thu 01.10.09	Wed 14.10.09	45			
47	<b>4.4 Reporting WP 4</b>	10 days	Thu 15.10.09	Wed 28.10.09	46			
48	<b>5.WP5.SELECTION OF TRAINING CANDIDATES AND SME's FOR PILOT RUN : 30 UNEMPLOYED YOUNG PEOPLE AND 30 SME's</b>	170 days	Mon 01.06.09	Fri 22.01.10				
49	<b>5.1.Preparation selection criterion for trainees and SME 's</b>	21 days	Mon 01.06.09	Mon 29.06.09				
50	5.1.1. Review and delivery of TIC questionnaire for SMEs	11 days	Mon 01.06.09	Mon 15.06.09	17FS+21 c			
51	5.1.2. Finalization of the Questionary for Analyzing SME's Needs	10 days	Tue 16.06.09	Mon 29.06.09	50			
52	<b>5.2.Making announcement through relevant channels</b>	10 days	Mon 28.09.09	Fri 09.10.09				
53	<b>5.3. Sending/ Collecting / Analyzing Questionnaires</b>	15 days	Mon 12.10.09	Fri 30.10.09	52			
54	<b>5.4. First selection of trainees</b>	20 days	Mon 02.11.09	Fri 27.11.09	53			
55	<b>5.5. Interview of the trainees</b>	30 days	Mon 30.11.09	Fri 08.01.10	54			
56	<b>5.6. Meeting with potential SME's</b>	30 days	Mon 12.10.09	Fri 20.11.09	52			
57	<b>5.7 Identification of SME's</b>	10 days	Mon 23.11.09	Fri 04.12.09	56			
58	<b>5.8 Reporting WP5</b>	10 days	Mon 11.01.10	Fri 22.01.10	57;55			
59	<b>6.WP6.DEVELOPMENT OF TESTING AND ASSESMENT MODEL</b>	62 days	Tue 15.12.09	Wed 10.03.10				
60	<b>6.1.Development of the testing and assesment model</b>	20 days	Tue 15.12.09	Mon 11.01.10				


Project: AJOY  
Date: Mon 01.06.09

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	

ID	Task Name	Duration	Start	Finish	Predecessor	Task Type		
						FSS	T	TFS
61	6.1.1.Collecting best practices and other procedures for testing and certification from partners	10 days	Tue 15.12.09	Mon 28.12.09	33			
62	6.1.2.Analysis of the Partners' Reports	10 days	Tue 29.12.09	Mon 11.01.10	61			
63	<b>6.2.TESTING and CERTIFICATION</b>	<b>30 days</b>	<b>Tue 12.01.10</b>	<b>Mon 22.02.10</b>				
64	6.2.1 Preparation of Draft Testing and Certification Model	15 days	Tue 12.01.10	Mon 01.02.10	62			
65	6.2.2.Feedbacks for testing and certification model from partners	5 days	Tue 02.02.10	Mon 08.02.10	64			
66	6.2.3 Revision of the testing model	10 days	Tue 09.02.10	Mon 22.02.10	65			
67	<b>6.4 Dissemination of the testing model</b>	<b>12 days</b>	<b>Tue 23.02.10</b>	<b>Wed 10.03.10</b>				
68	6.4.1. Translation of the Model in partners' language	10 days	Tue 23.02.10	Mon 08.03.10	66			
69	6.4.2.Publication of developed model on the web-site	2 days	Tue 09.03.10	Wed 10.03.10	68			
70	<b>6.5 Reporting the WP 6</b>	<b>10 days</b>	<b>Tue 23.02.10</b>	<b>Mon 08.03.10</b>	<b>66</b>			
71	<b>7.WP7.PILOTING OF THE MODEL: TRAINING DELIVERY</b>	<b>65 days</b>	<b>Mon 04.01.10</b>	<b>Fri 02.04.10</b>				
72	<b>7.1 Preparing Learning Environments</b>	<b>10 days</b>	<b>Mon 04.01.10</b>	<b>Fri 15.01.10</b>	<b>64SF</b>			
73	<b>7.2.Training of the selected target groups</b>	<b>22 days</b>	<b>Mon 18.01.10</b>	<b>Tue 16.02.10</b>	<b>72</b>			
74	<b>7.3. Internships of the trained trainees</b>	<b>20 days</b>	<b>Mon 22.02.10</b>	<b>Fri 19.03.10</b>	<b>73</b>			
75	<b>7.4 Reporting the WP 7</b>	<b>10 days</b>	<b>Mon 22.03.10</b>	<b>Fri 02.04.10</b>	<b>74</b>			
76	<b>8.WP8.EVALUATION AND MONITORING</b>	<b>431 days</b>	<b>Wed 29.04.09</b>	<b>Wed 22.12.10</b>				
77	<b>8.1.Study Visits</b>	<b>49 days</b>	<b>Wed 17.02.10</b>	<b>Mon 26.04.10</b>				
78	8.1.1 First Study Visit	3 days	Wed 17.02.10	Fri 19.02.10	73			
79	8.1.2 Second study visit	3 days	Thu 22.04.10	Mon 26.04.10	94			
80	<b>8.2.Preperation of Questionnaires</b>	<b>21 days</b>	<b>Fri 01.05.09</b>	<b>Fri 29.05.09</b>	<b>17</b>			
81	<b>8.3.(Evaluation report on project activities) (Same as with 8.6)</b>	<b>10 days</b>	<b>Mon 16.11.09</b>	<b>Fri 27.11.09</b>				
82	<b>8.4 Evaluation of WP Reports</b>	<b>193 days</b>	<b>Thu 29.10.09</b>	<b>Mon 26.07.10</b>				
83	8.4.1. Analysis of WP3	3 days	Tue 29.12.09	Thu 31.12.09	34			
84	8.4.2. Analysis of WP4	3 days	Thu 29.10.09	Mon 02.11.09	47			
85	8.4.3. Analysis of WP5	3 days	Mon 25.01.10	Wed 27.01.10	58			
86	8.4.4. Analysis of WP6	3 days	Tue 09.03.10	Thu 11.03.10	70			
87	8.4.5. Analysis of WP7	3 days	Mon 05.04.10	Wed 07.04.10	75			
88	8.4.6. Analysis of WP9	3 days	Thu 03.06.10	Mon 07.06.10	99			
89	8.4.7. Analysis of WP10	3 days	Thu 22.07.10	Mon 26.07.10	104			
90	<b>8.5 Evaluation of Web site usage of Project</b>	<b>431 days</b>	<b>Wed 29.04.09</b>	<b>Wed 22.12.10</b>	<b>24</b>			
91	<b>8.6 Preparation of Interim Evaluation Report</b>	<b>10 days</b>	<b>Mon 16.11.09</b>	<b>Fri 27.11.09</b>				
92	<b>8.7 Preparation of Final Evaluation Report</b>	<b>10 days</b>	<b>Mon 18.10.10</b>	<b>Fri 29.10.10</b>				
93	<b>9.WP9.TESTING AND CERTIFICATION:"EUROPEAN COMPUTER DRIVING LICENCE"</b>	<b>53 days</b>	<b>Thu 01.04.10</b>	<b>Mon 14.06.10</b>				
94	9.1.Theoretical and practical test	15 days	Thu 01.04.10	Wed 21.04.10	74			
95	9.2 Awarding succesful trainees	3 days	Mon 17.05.10	Wed 19.05.10	94			
96	<b>9.3.Common Certificates</b>	<b>18 days</b>	<b>Thu 20.05.10</b>	<b>Mon 14.06.10</b>				
97	9.3.1 Preparation of certificates	10 days	Thu 20.05.10	Wed 02.06.10	95			
98	9.3.2.Publication of certificate	8 days	Thu 03.06.10	Mon 14.06.10	97			
99	9.4 Reporting WP9	10 days	Thu 20.05.10	Wed 02.06.10	95			
100	<b>10.WP10.REVISION OF THE MODEL PILOTED</b>	<b>45 days</b>	<b>Thu 03.06.10</b>	<b>Wed 04.08.10</b>				
101	<b>10.1 Revision of a coordinated model</b>	<b>45 days</b>	<b>Thu 03.06.10</b>	<b>Wed 04.08.10</b>				
102	10.1.1 Revision of Training Programmes and testing model	15 days	Thu 03.06.10	Wed 23.06.10	99			
103	10.1.2 Commenting on the revised programmes and testing model	10 days	Thu 24.06.10	Wed 07.07.10	102			
104	10.1.3 Finalizing coordinated model	10 days	Thu 08.07.10	Wed 21.07.10	103			
105	10.2 Reporting WP 10	10 days	Thu 22.07.10	Wed 04.08.10	104			



Project: AJOY Date: Mon 01.06.09	Task		Milestone		External Tasks	
	Split		Summary		External MileTask	
	Progress		Project Summary		Split	

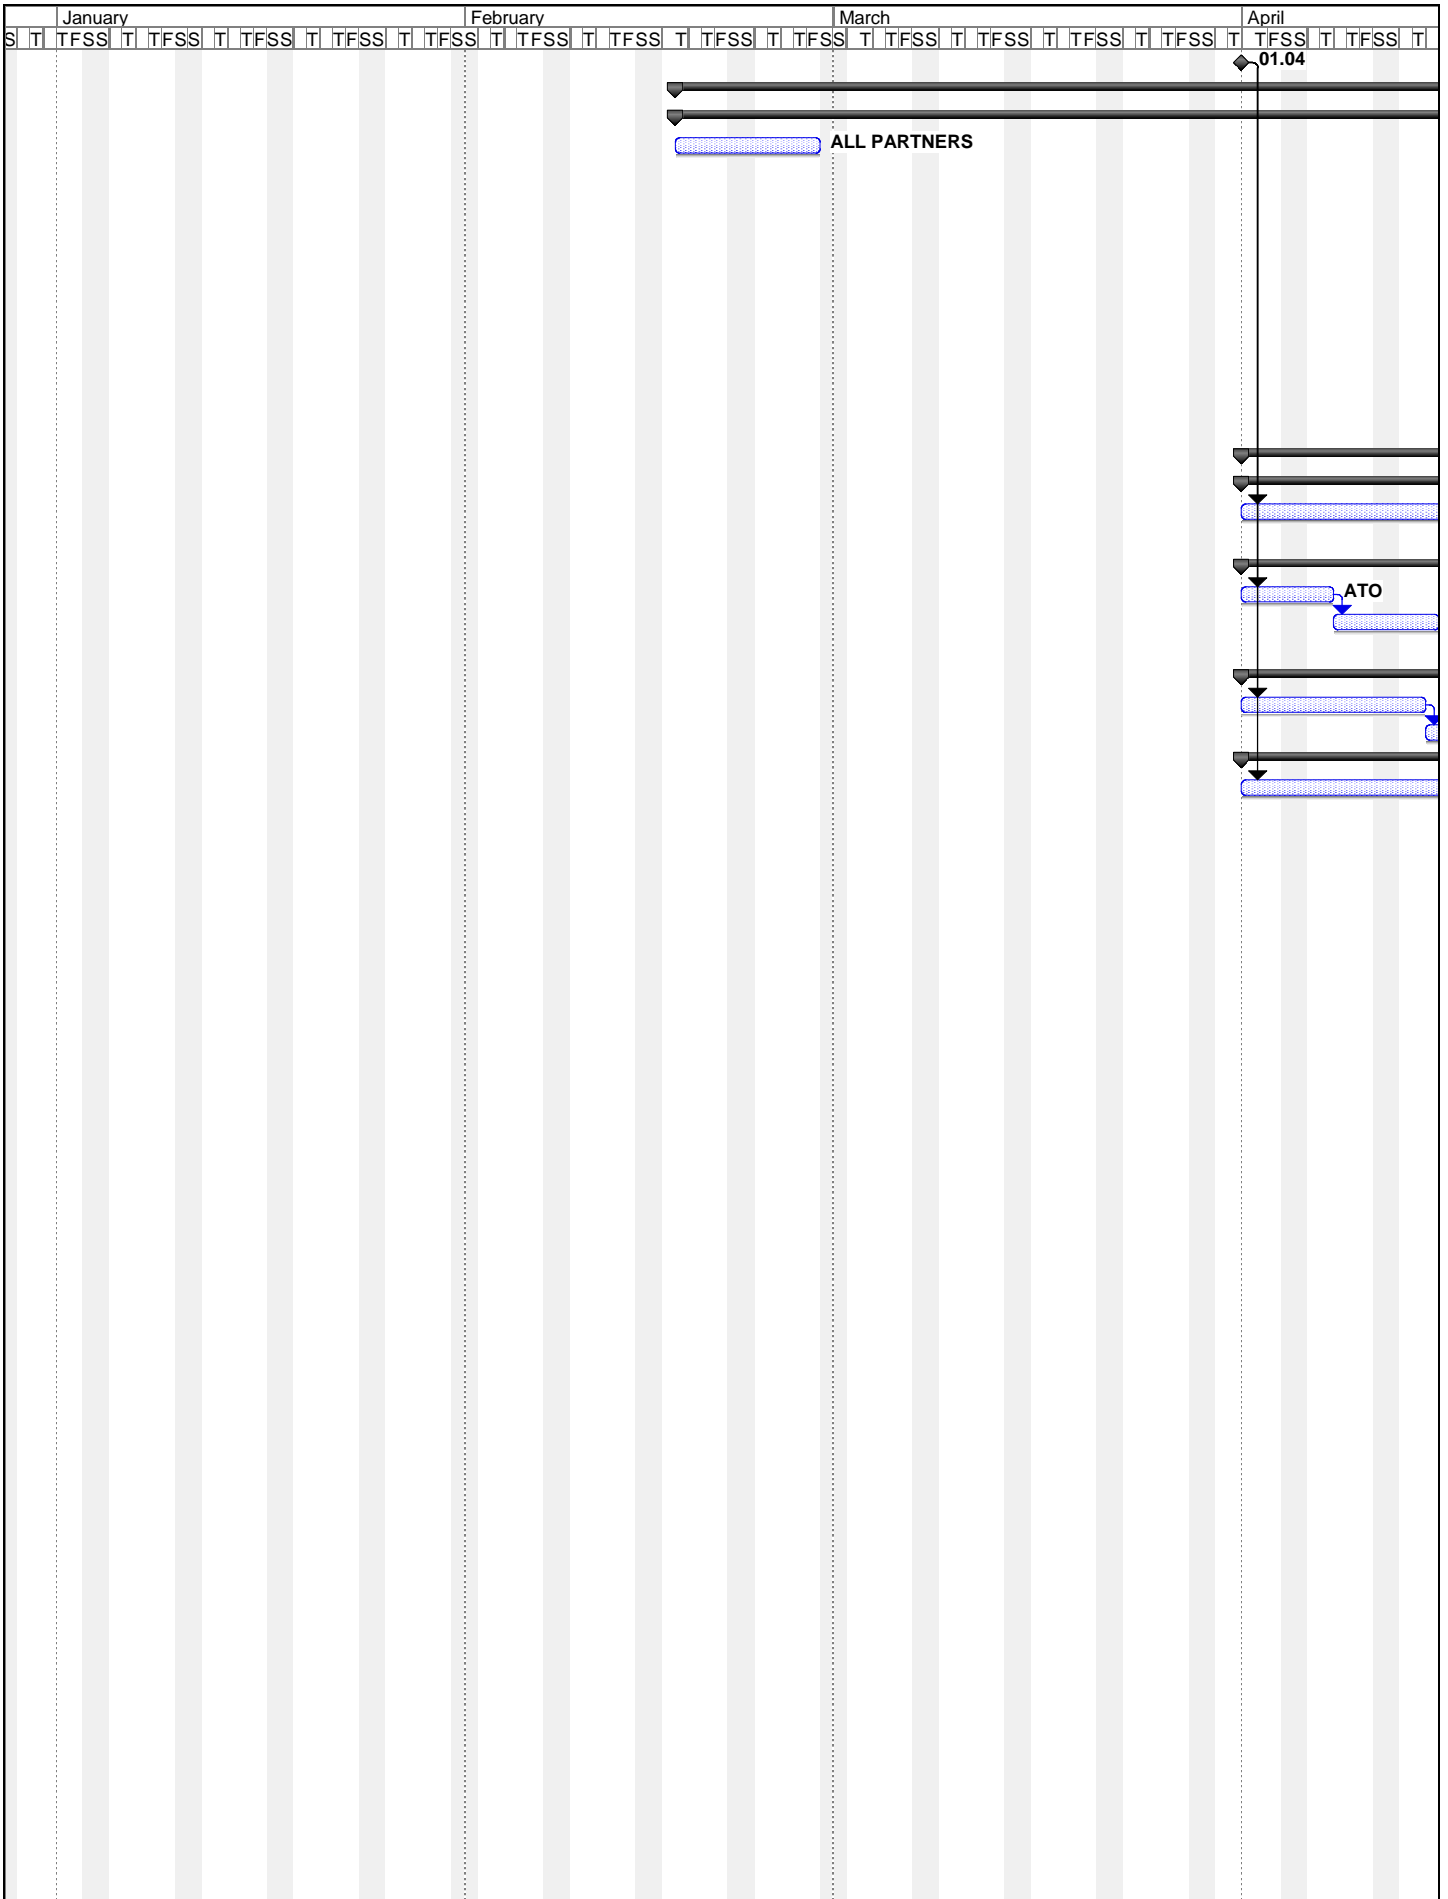










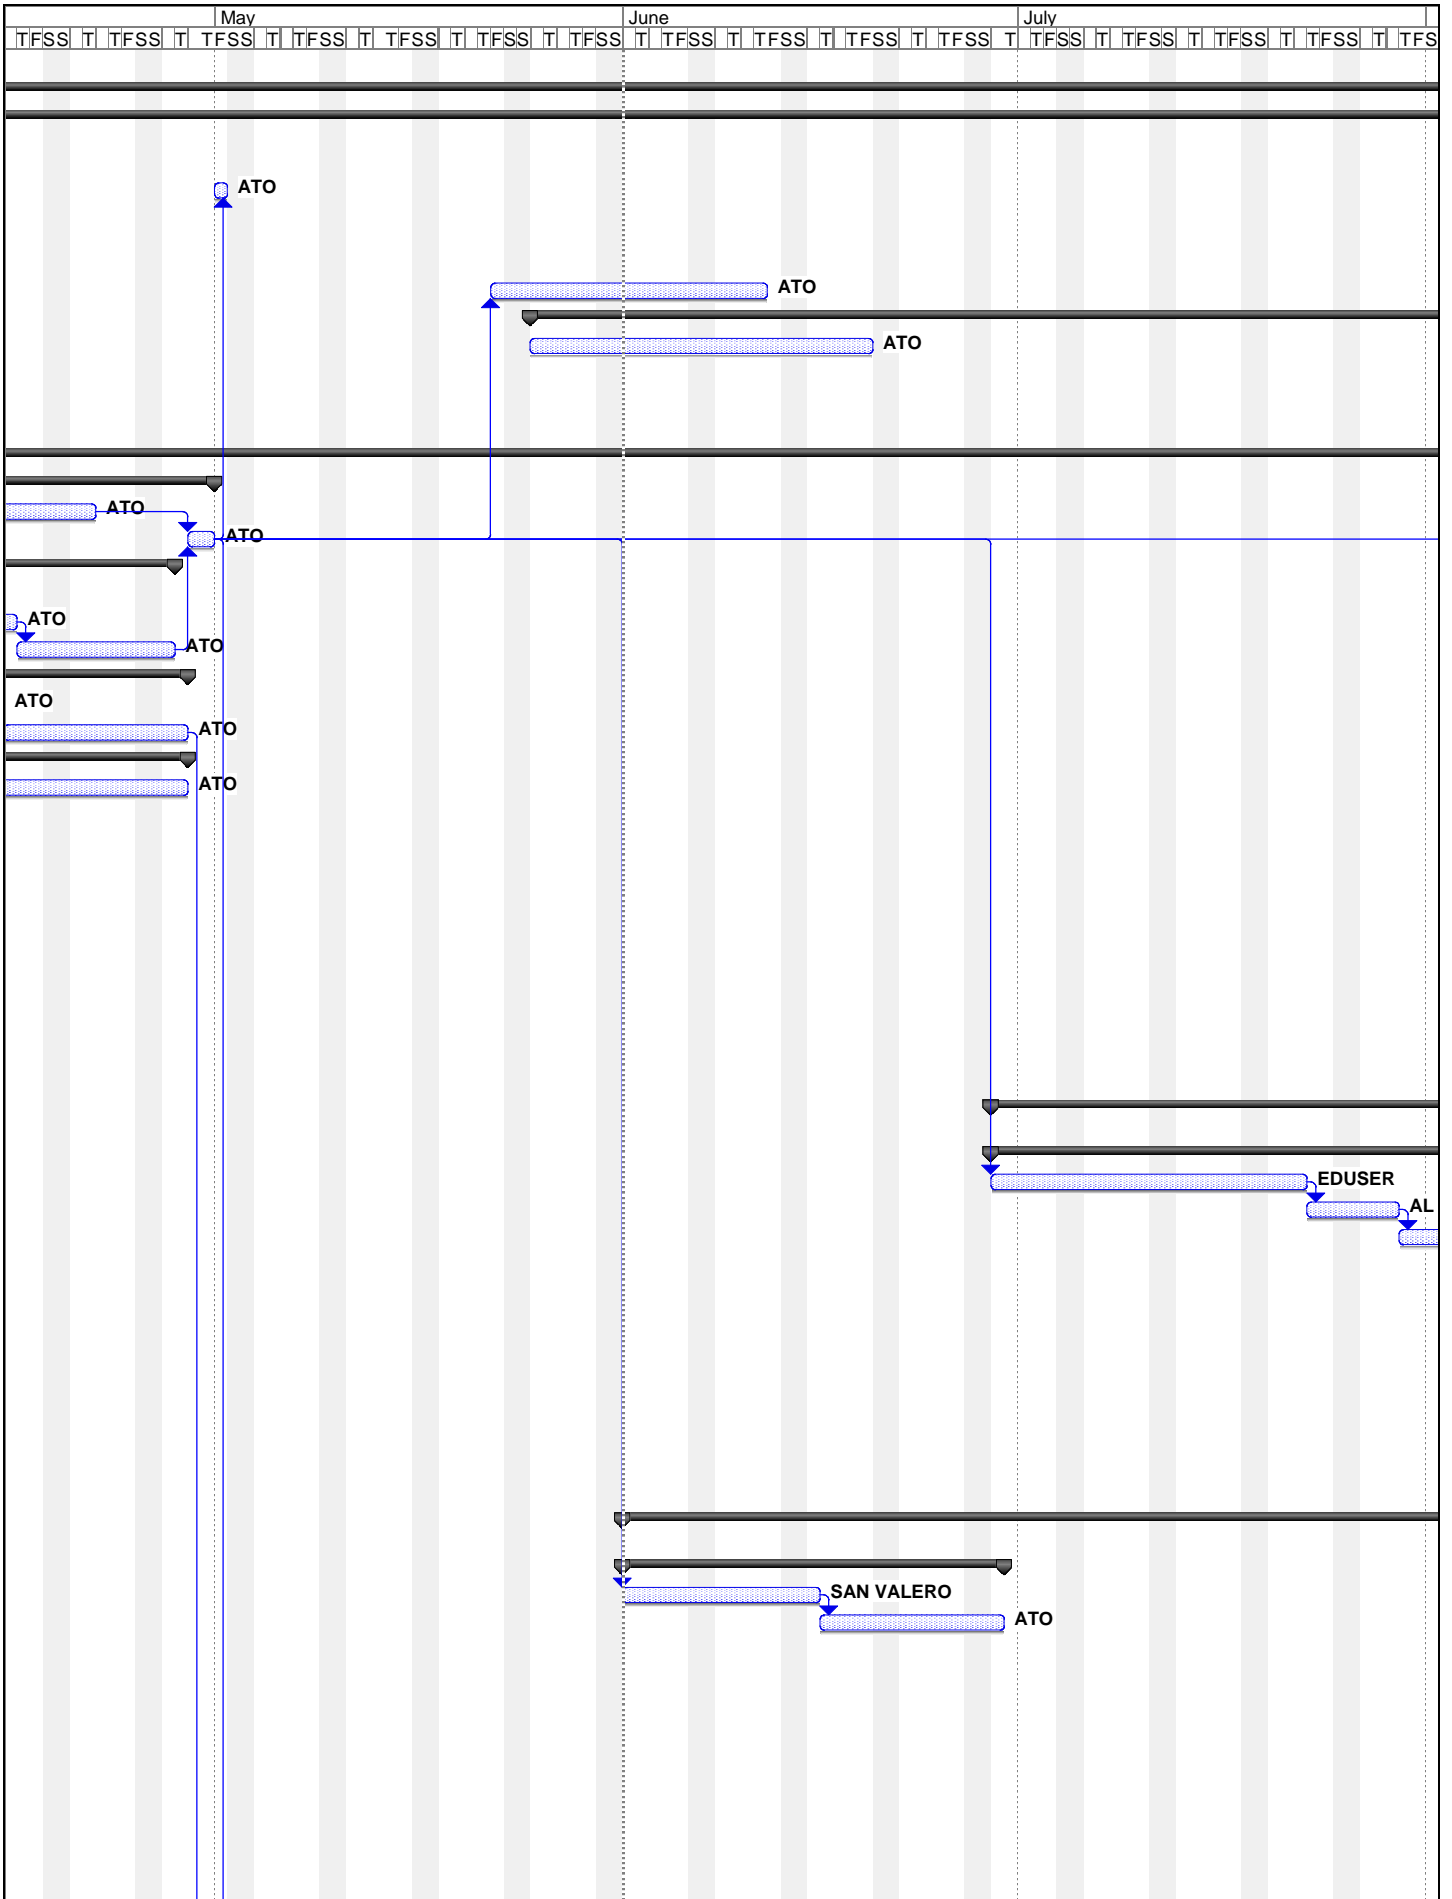
Project: AJOY  
Date: Mon 01.06.09

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	

January							February							March							April								
S	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T	TFSS	T

--	--	--	--

Project: AJOY Date: Mon 01.06.09	Task		Milestone		External Tasks	
	Split		Summary		External MileTask	
	Progress		Project Summary		Split	




Project: AJOY  
Date: Mon 01.06.09

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	






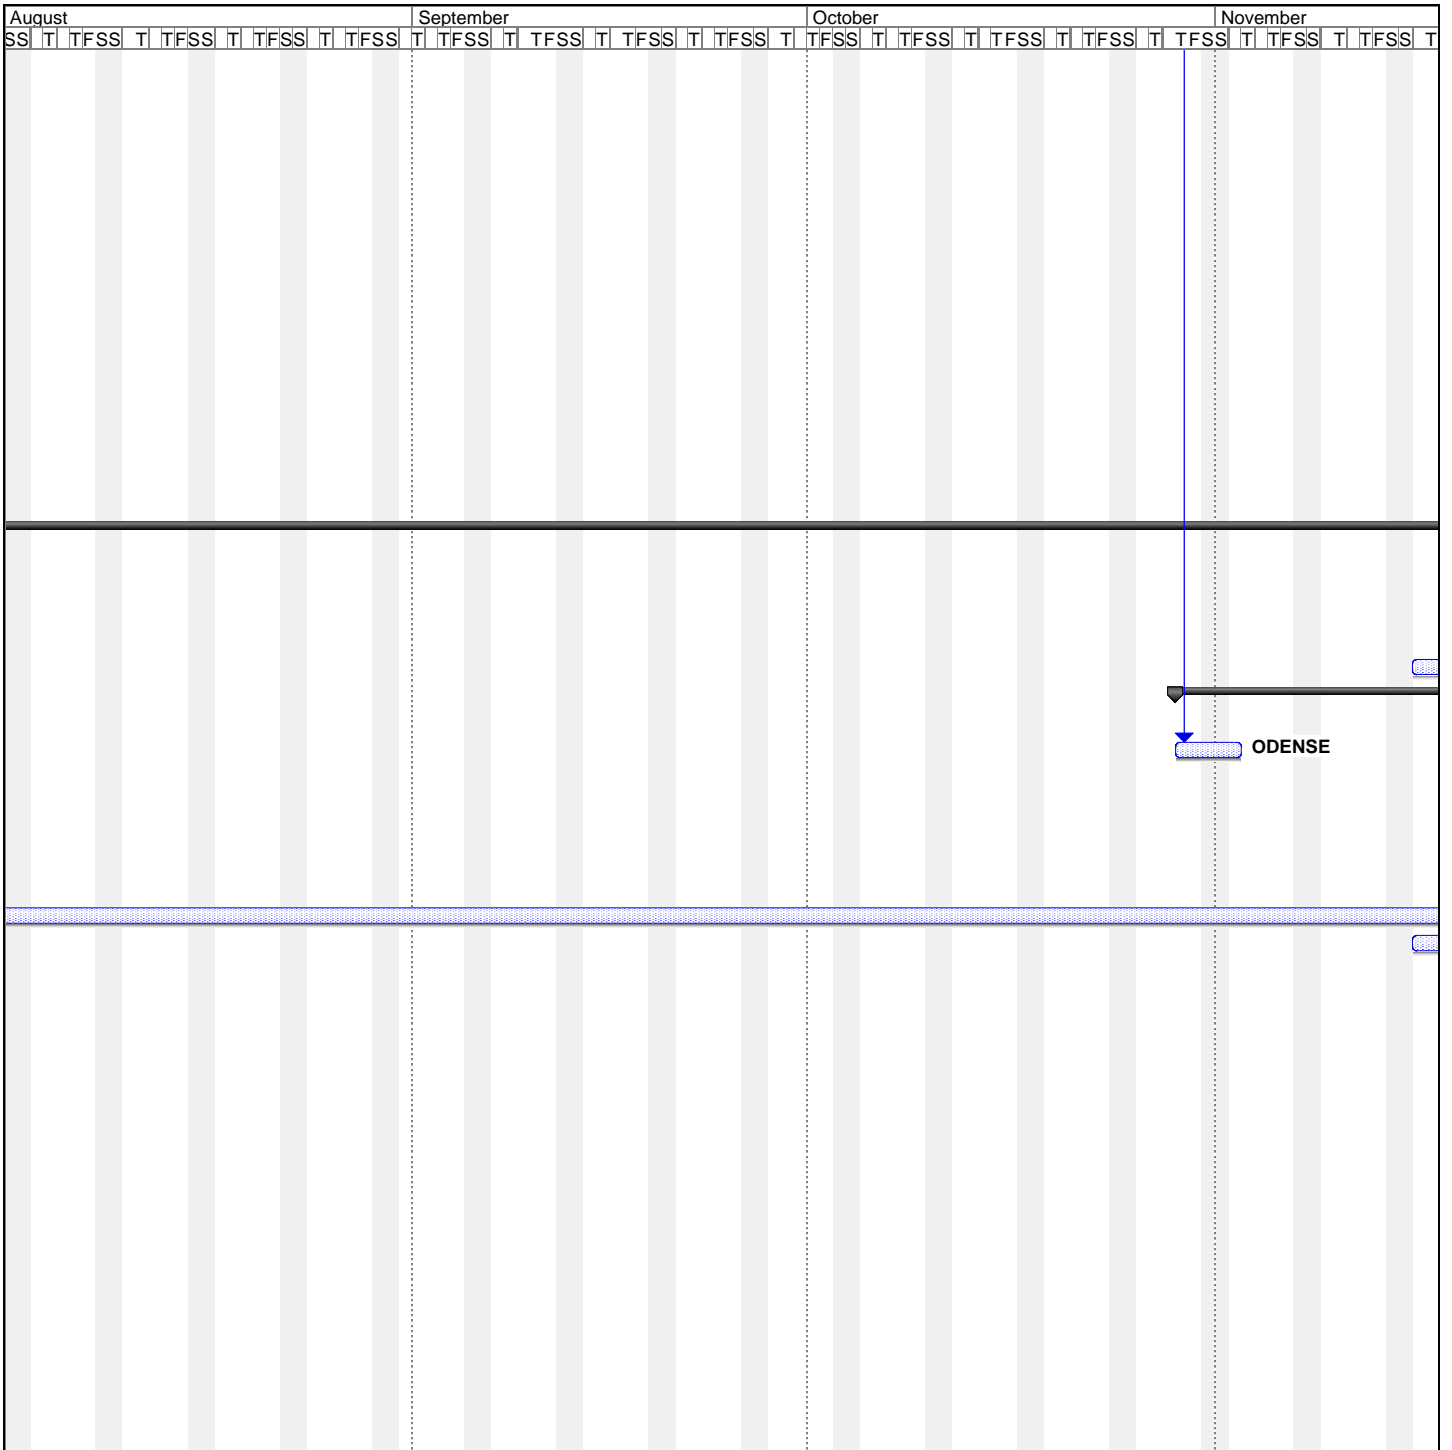

Project: AJOY  
Date: Mon 01.06.09

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	




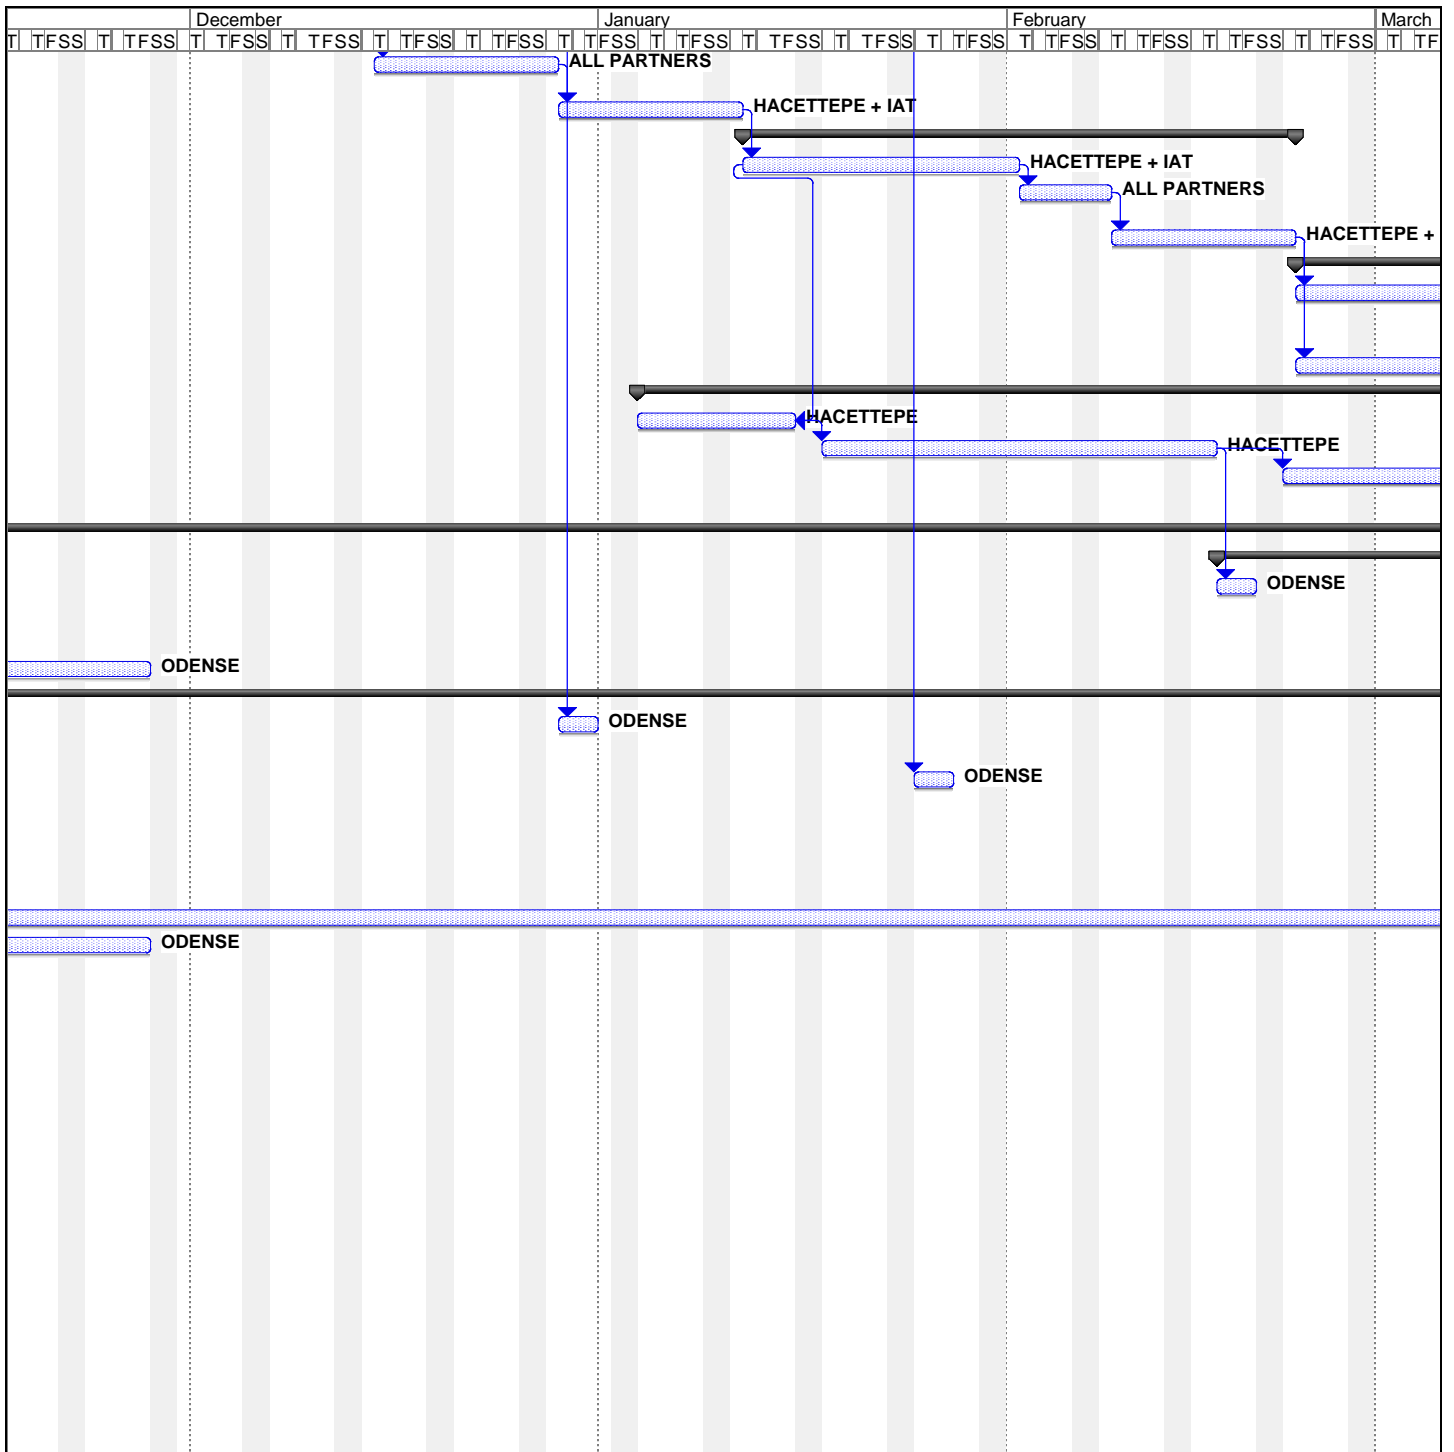


Project: AJOY  
Date: Mon 01.06.09

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	



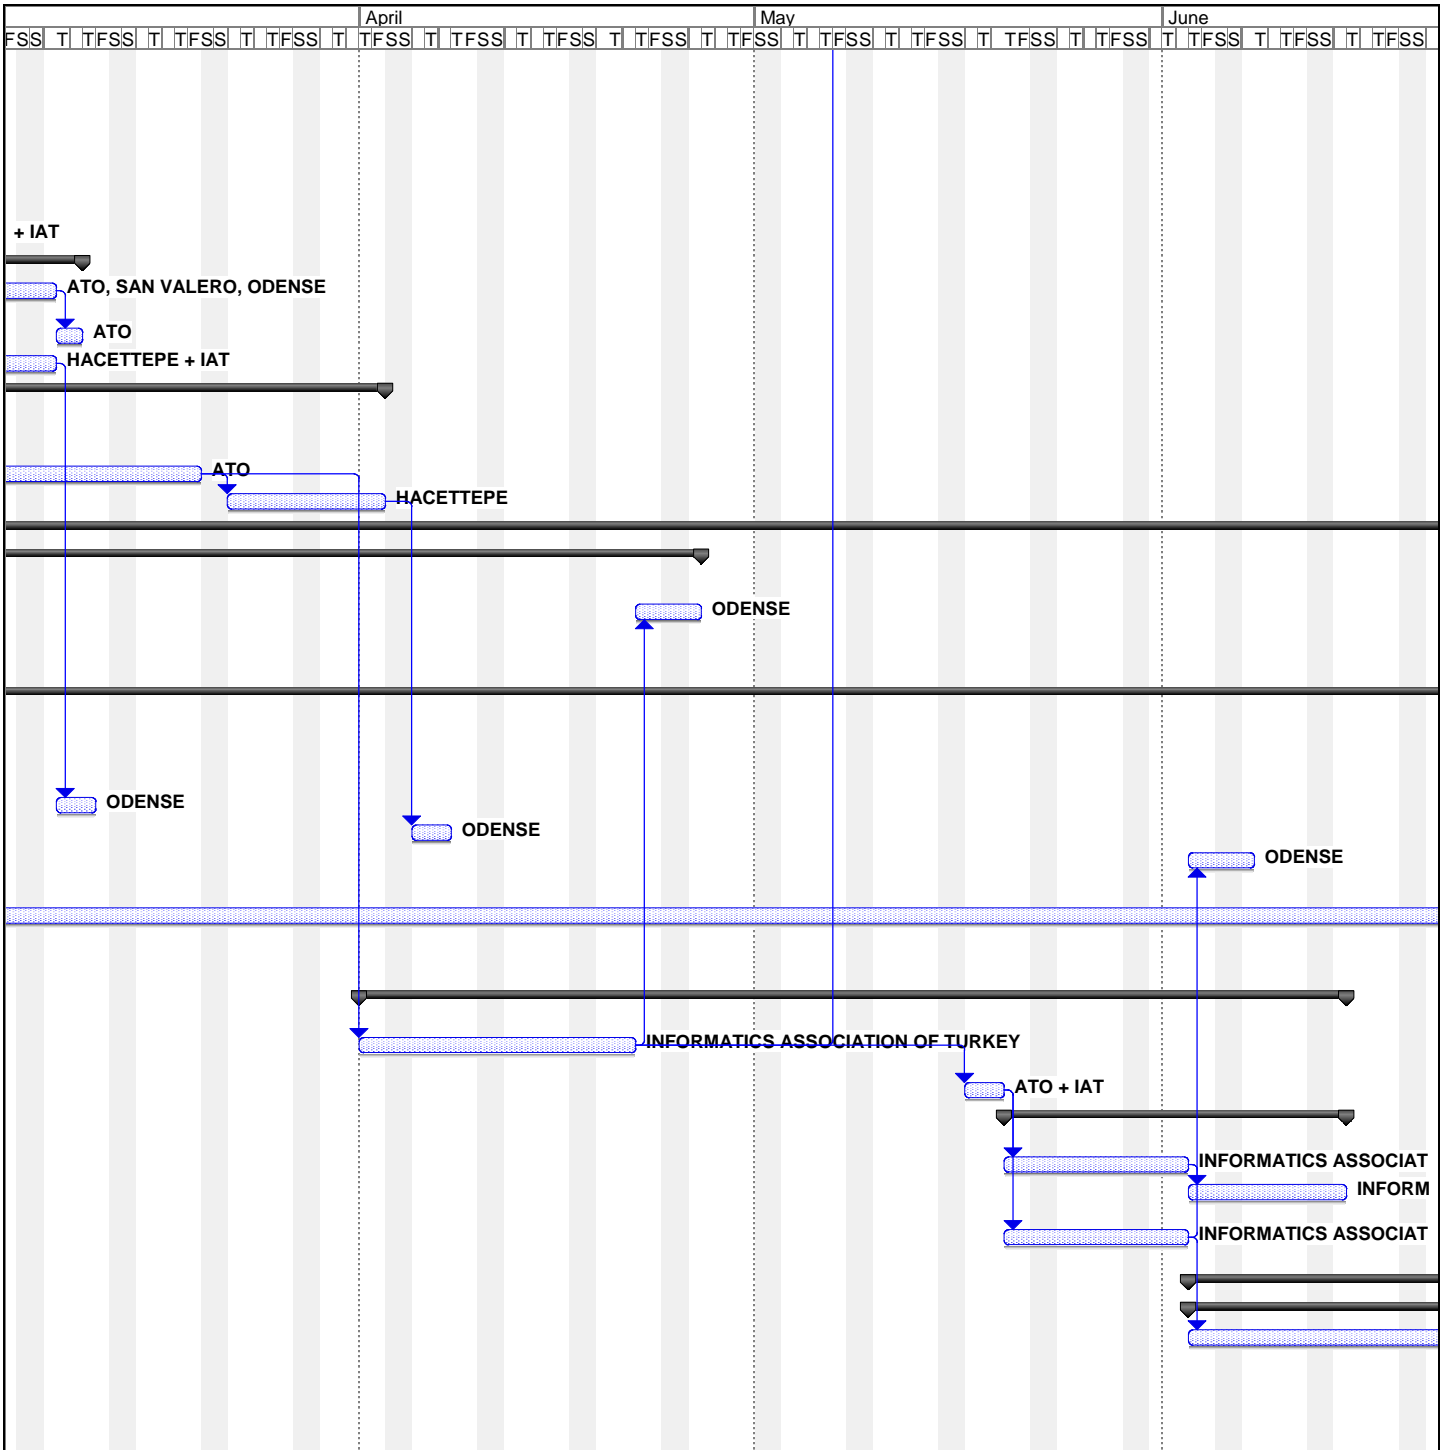




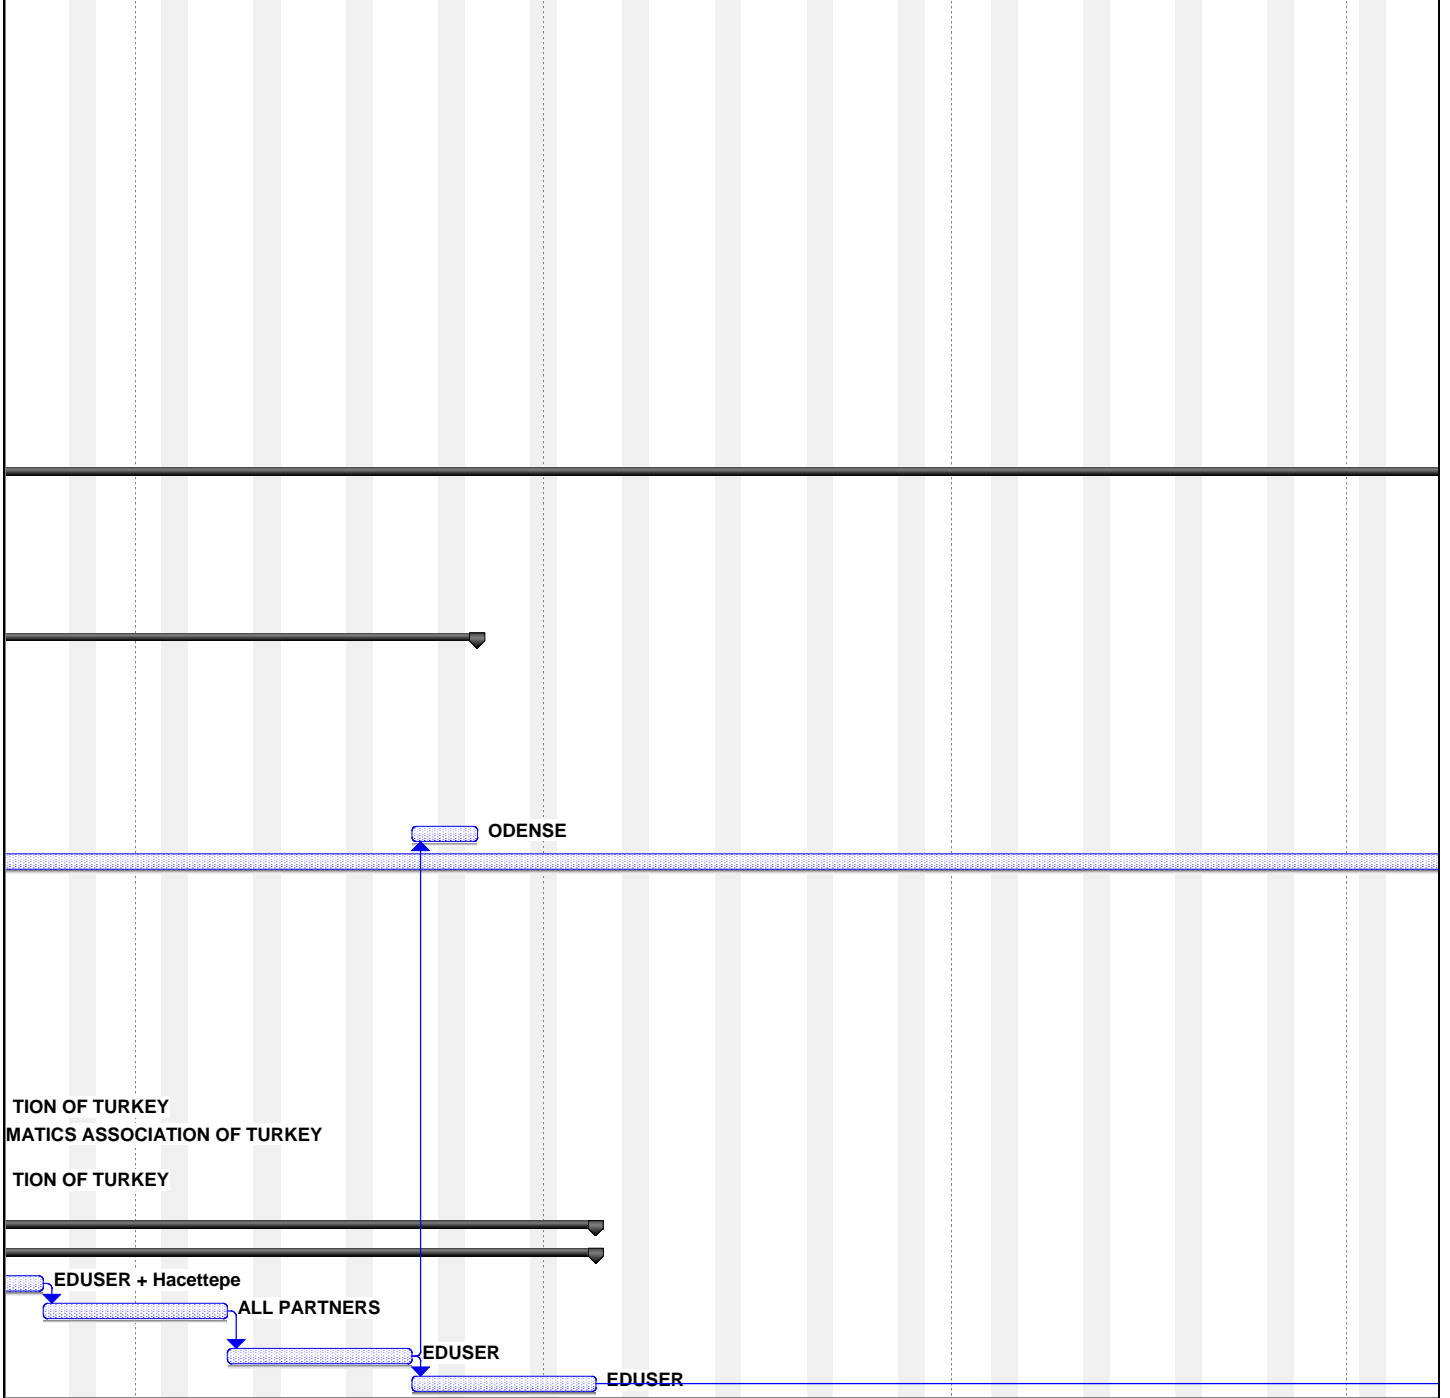



TION OF TURKEY  
 MATICS ASSOCIATION OF TURKEY  
 TION OF TURKEY

Project: AJOY Date: Mon 01.06.09	Task		Milestone		External Tasks	
	Split		Summary		External MileTask	
	Progress		Project Summary		Split	

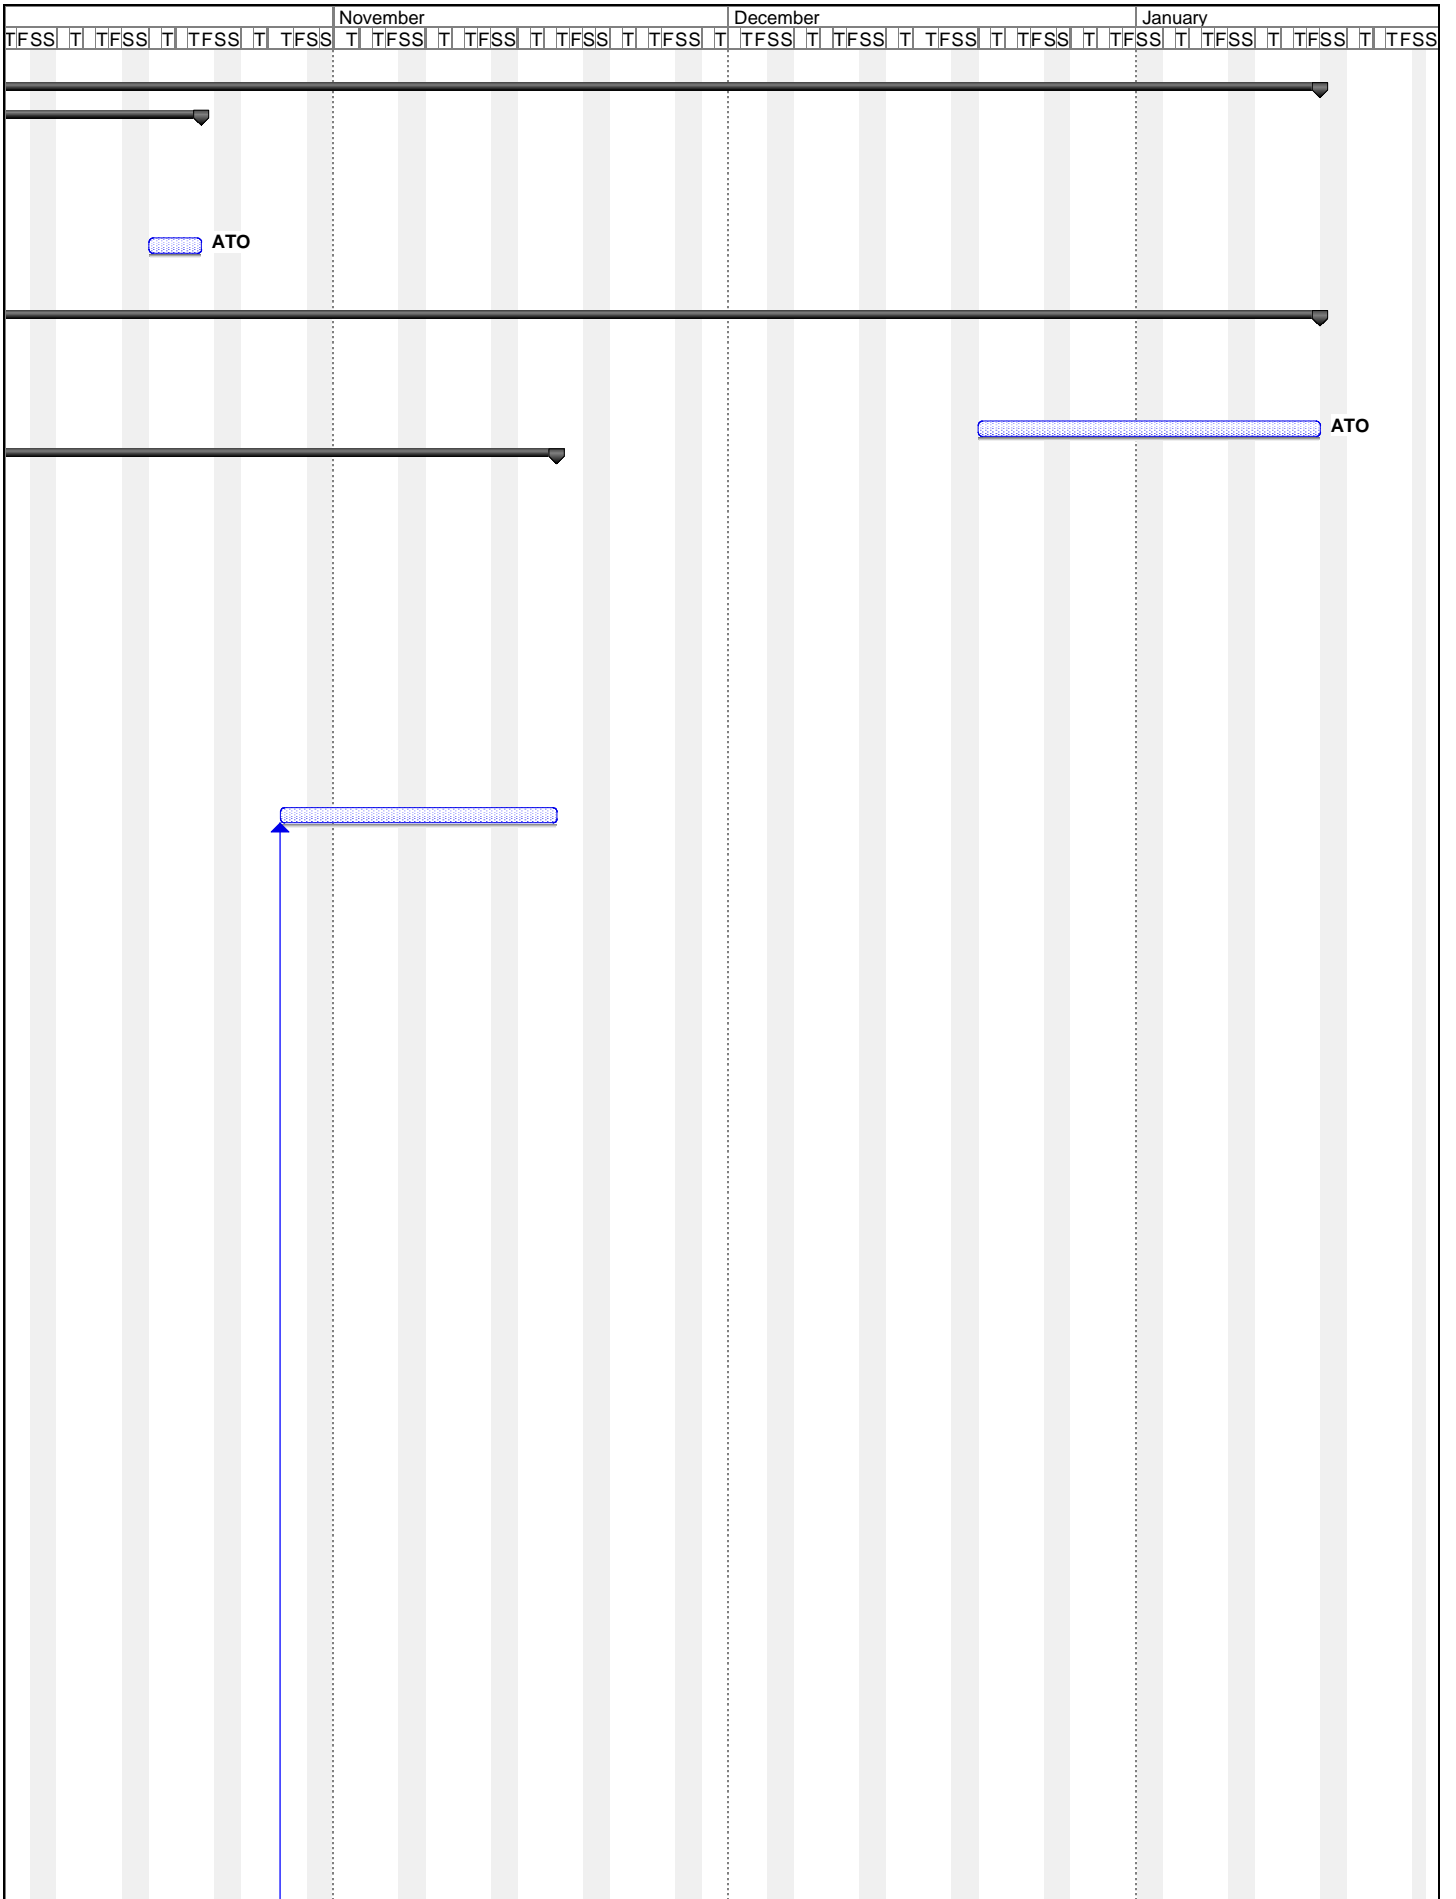

Project: AJOY  
Date: Mon 01.06.09

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	

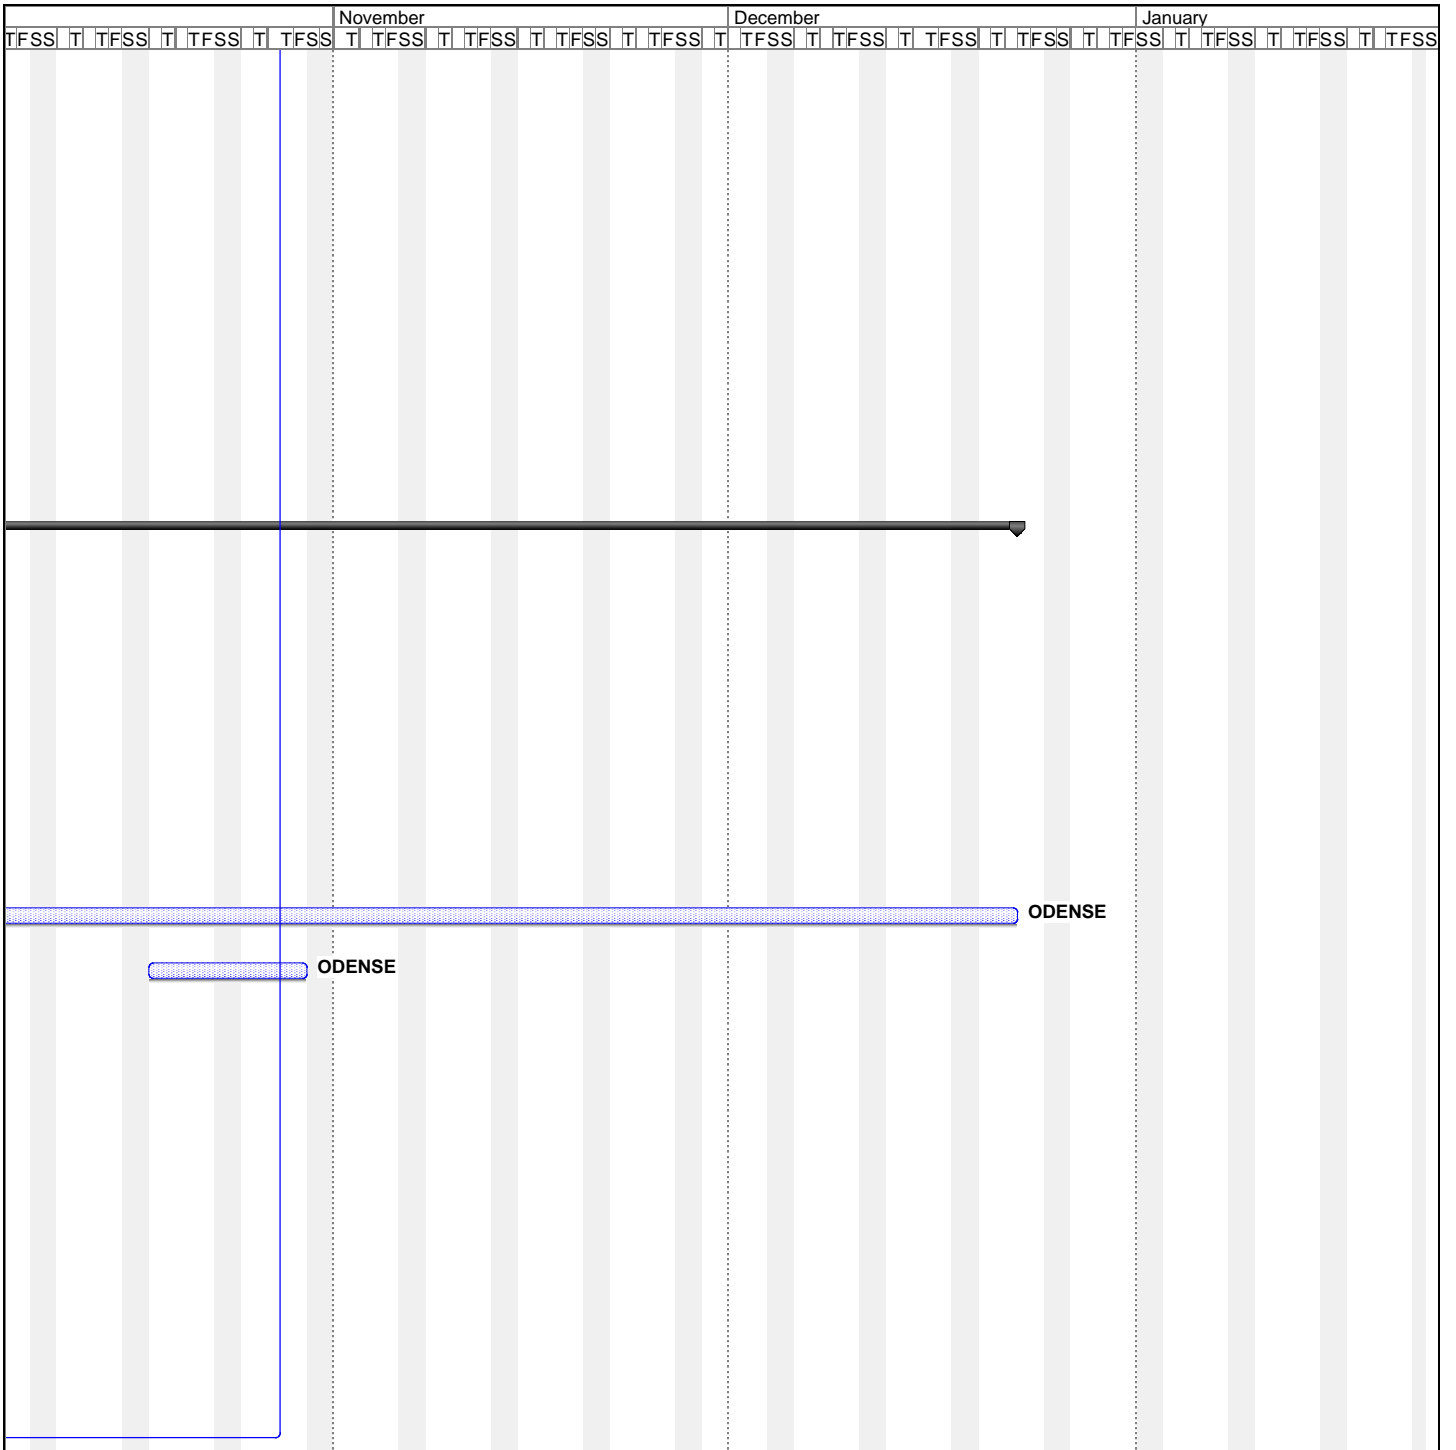

Project: AJOY Date: Mon 01.06.09	Task		Milestone		External Tasks	
	Split		Summary		External MileTask	
	Progress		Project Summary		Split	
